



HPO - Interim Protection at Lakefront Airport and Stars & Stripes Floodwalls, Orleans.

Progress Photographs



US Army Corps
of Engineers®

HPO Stars and Stripes Floodwall, Orleans



Hesco Basket (3'x3'x4') with angle support along the floodwall on the side of Leon C. Simon Road is completed.



US Army Corps
of Engineers®

HPO Stars and Stripes Floodwall, Orleans




Generator, on the left, supplying power to drill the holes in the concrete and to anchor the angles with bolts. On the right, Bobcat bringing the materials to the job.



US Army Corps
of Engineers®

HPO Stars and Stripes Floodwall, Orleans

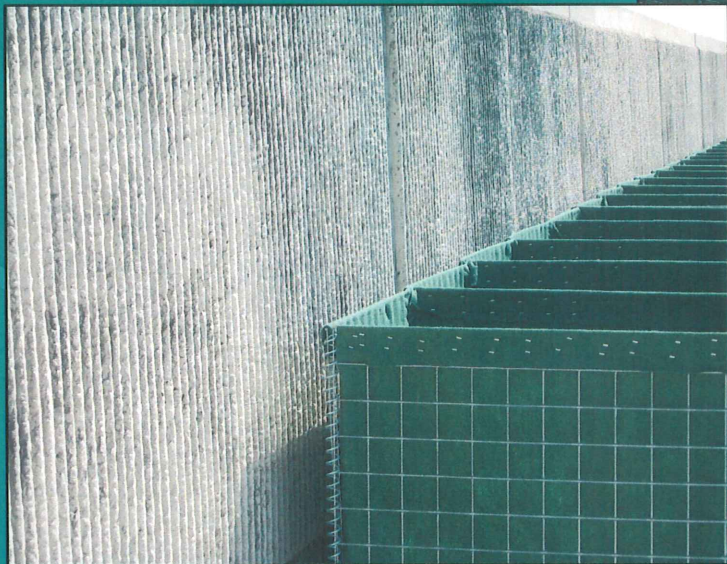

Hesco basket installation is in progress at the Hayne Blvd. along the Stars & Stripes flood wall.



US Army Corps
of Engineers®

HPO Stars and Stripes Floodwall, Orleans



Baskets are getting filled with stones on the right. Front end loader is bringing the stones to fill the basket. Stones are stockpiled under the bridge.



US Army Corps
of Engineers®

HPO Stars and Stripes Floodwall, Orleans



Stone filling in the basket at the Hayne Blvd. is progressing as on August 27, 2007. The stone material is pumped, vibrated, and placed in the baskets through the conveyor.



US Army Corps
of Engineers®

HPO Stars and Stripes Floodwall, Orleans



The stone spreader is ready for refill.




One lane is open for traffic when the work is in progress.

The stone spreader is on the bridge ramp and conveyor is extended up to the baskets due to the limited working space at the baskets. Six baskets are filled one time (+/- 15 tons of stone).



HPO Stars and Stripes Floodwall, Orleans

Interim concrete scour slab (9'x26') is extended between the Seabrook Bridge and I-Wall to provide an anchoring surface for the hesco baskets.

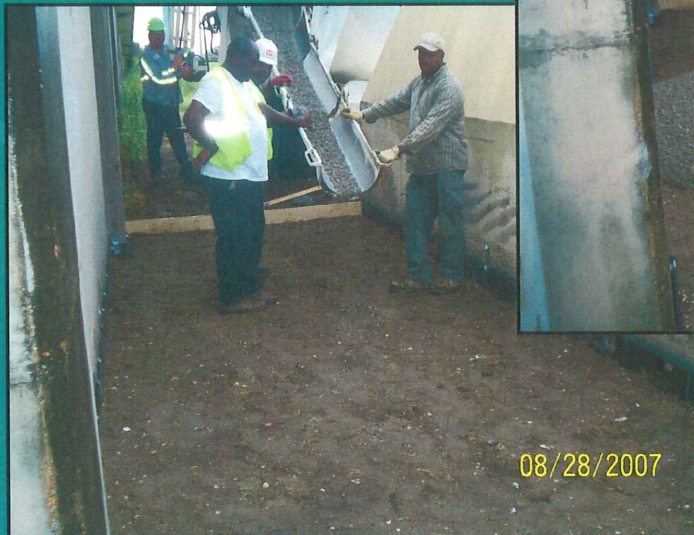

Stone filled hesco baskets are anchored to the newly poured slab



US Army Corps
of Engineers®

HPO Stars and Stripes Floodwall, Orleans

Project is substantially
completed on
September 5, 2007





US Army Corps
of Engineers®

HPO Stars and Stripes Floodwall, Orleans



Final inspection performed
on September 12, 2007.

Participants:

HPO Team, Orleans Levee
District Team, and
LADOTD Team.

